
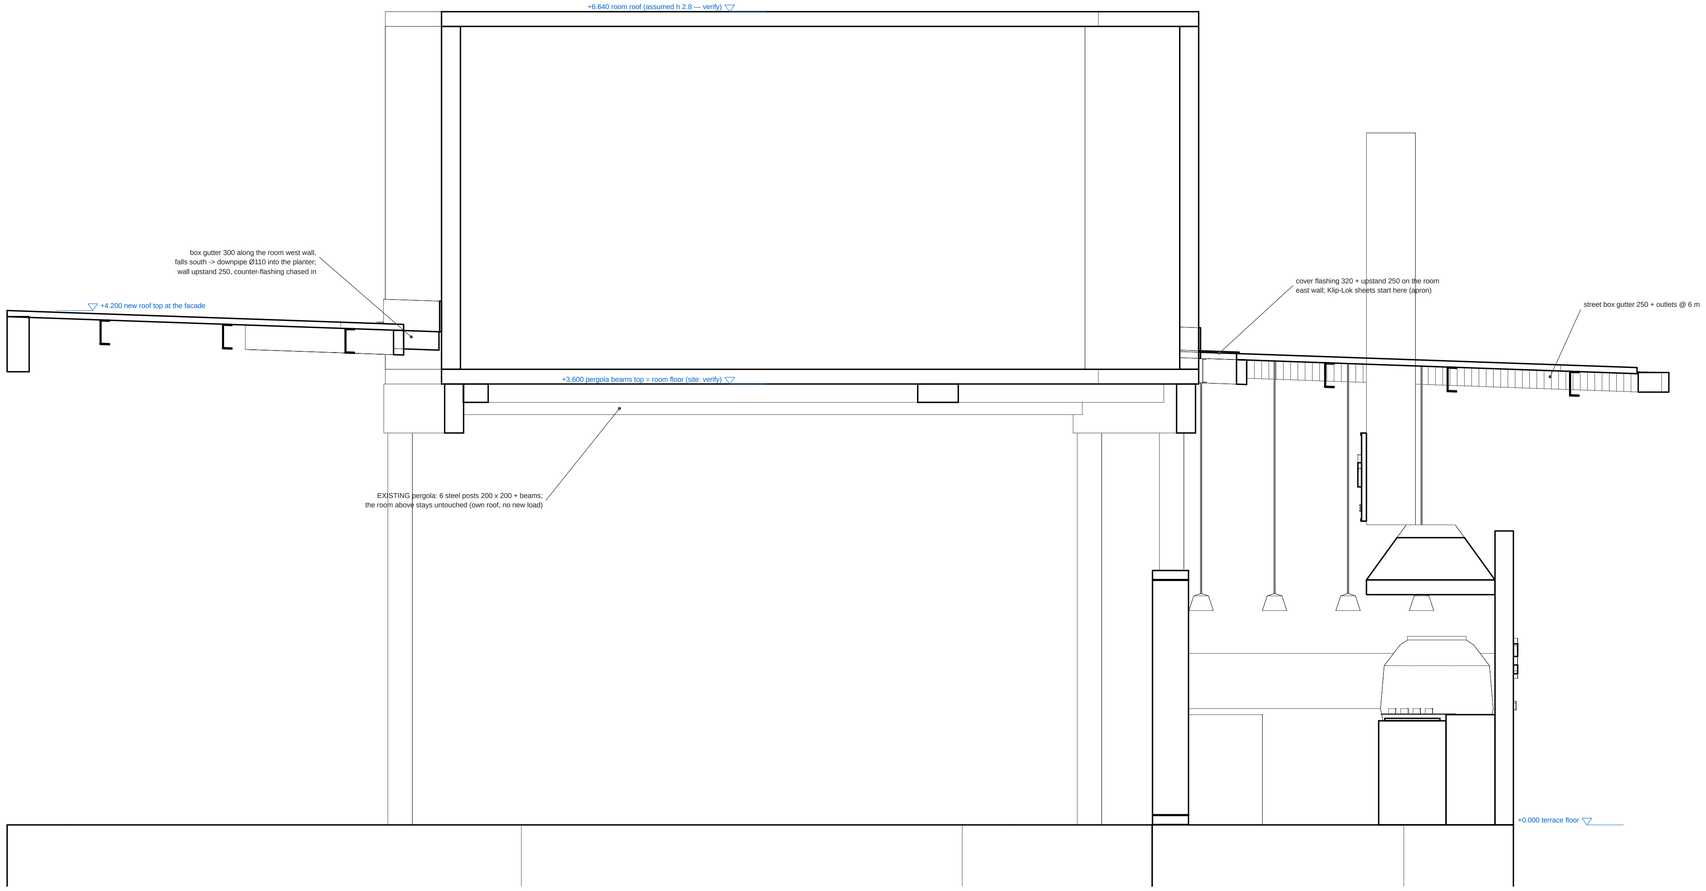


SECTION E-E THROUGH THE PERGOLA AND THE ROOM ABOVE (building → street) 1:25

new roof stops 300 off the room walls: box gutter on the up-slope (west) wall, cover flashing on the down-slope (east) wall

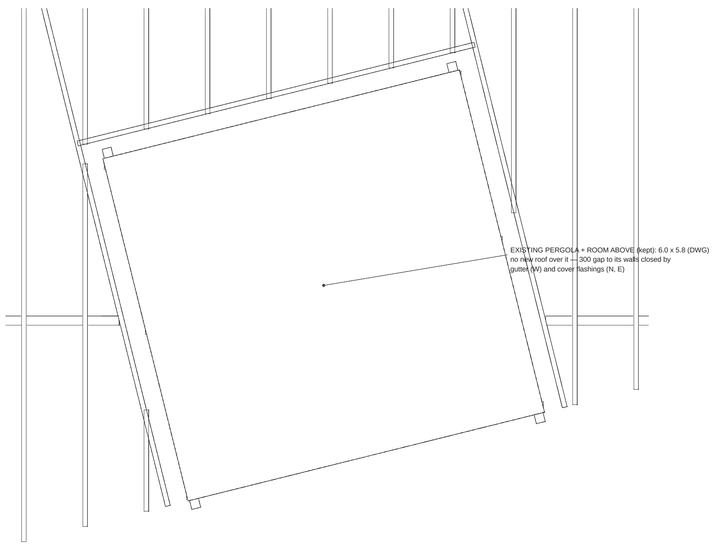

FRAMING PLAN ROUND THE ROOM (roof sheet removed) 1:50

trimmers UPN 200: W and E from the boundary wall to beam B, N between them; purlins stop on the trimmers; beam A ends on W / E

SEQUENCE

1. Survey: room walls (line, plumb, height, finish), pergola posts + levels, the room roof drainage, the boundary wall (owner, thickness) for the trimmer brackets.
2. Facade ledger, roof beams IPE 300, street columns. Trimmers UPN 200 round the room (W, E: boundary-wall bracket -> beam A -> beam B; N between W and E). Grid-A beam ends on the W / E trimmers.
3. Purlins C200 @ 1000 stopping on the trimmers (cleats). Nothing is fixed to the pergola or the room.
4. Insulation blanket 50 mm foil-faced on safety mesh, Klip-Lok sheets roll-formed on site (west field: facade -> gutter at the room; east field: room wall -> street gutter).
5. Box gutter 300 along the room west wall (fall 1 % to the south) + downpipe into the planter; cover flashings + 250 upstands on the N and E walls, counter-flashing into a chased joint, butyl tape + PU sealant, laps >= 150.
6. Water test of the junction before the ceilings; inside: pergola posts clad as Khiva columns, beams in carved walnut, panels between the joists.

WHY THIS DETAIL

The pergola carries a closed room: the new roof cannot pass over it and must not load it -> the roof is cut round it on its own trimmers.
Up-slope wall (west) collects the water of the facade field -> box gutter; side and down-slope walls only need cover flashings.

SAMARKAND — Uzbek / Tajik restaurant terrace · 254 Vo Nguyen Giap, Da Nang

Existing pergola + closed room above (kept) — new roof cut round it: section, framing, junction

Drawn from the 3D model (closed-shell, QA-clean); dimensions in mm, levels in m from the finished terrace floor ±0.000

Sheet S-09 Rev R12-v8.3 2026-11-04 A1 Construction set — verify on site before fabrication
