
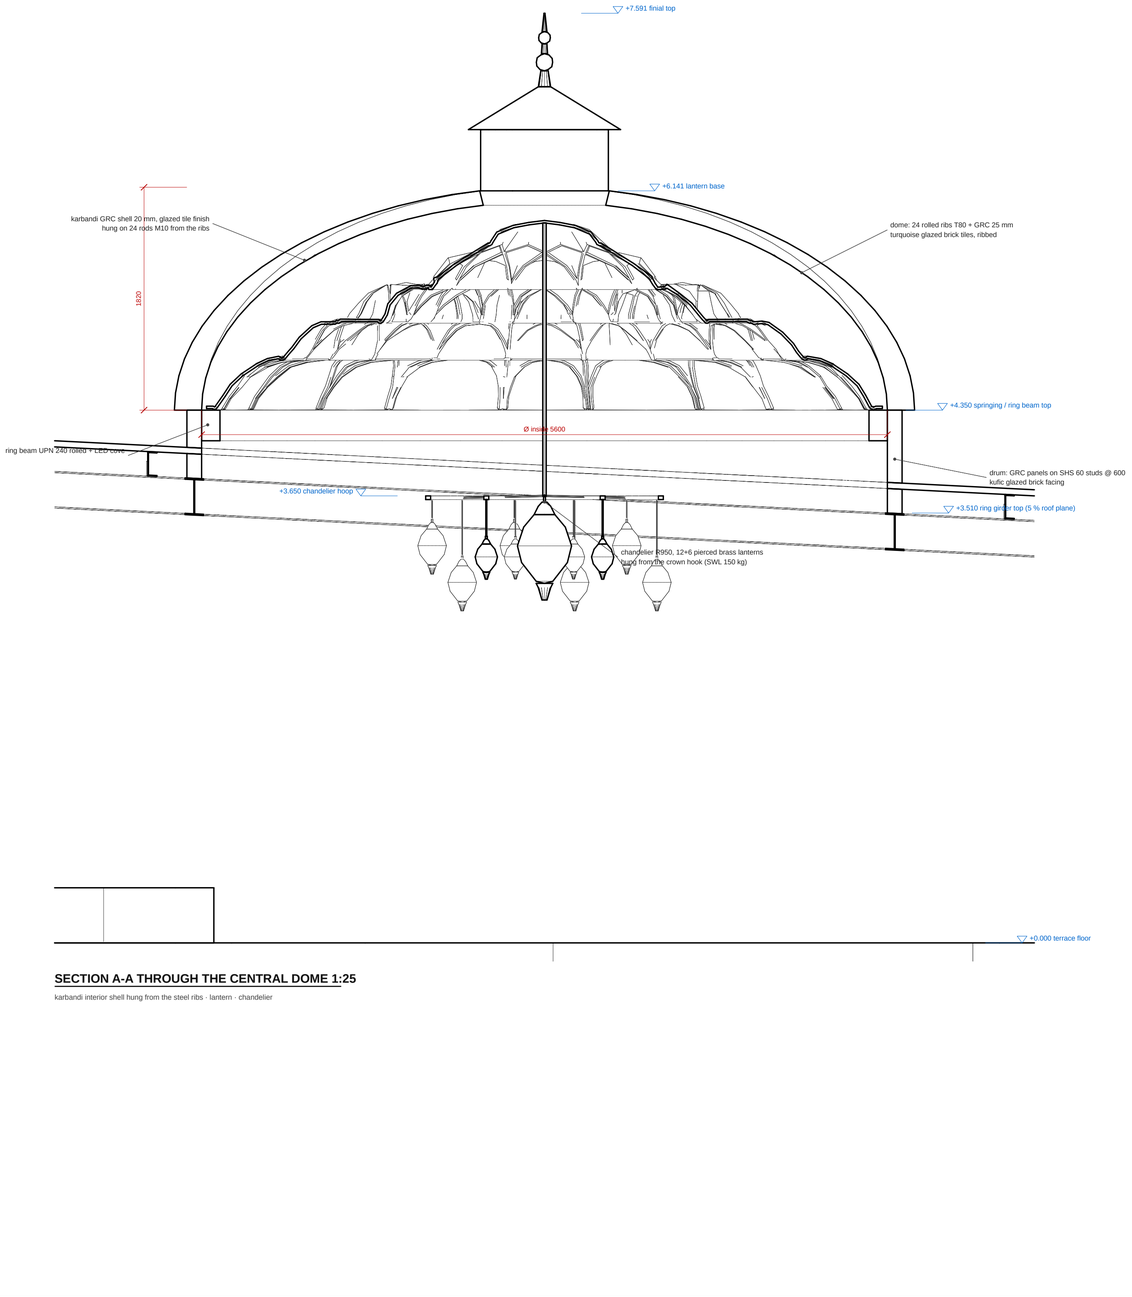


SECTION A-A THROUGH THE CENTRAL DOME 1:25

karbandi interior shell hung from the steel ribs · lantern · chandelier

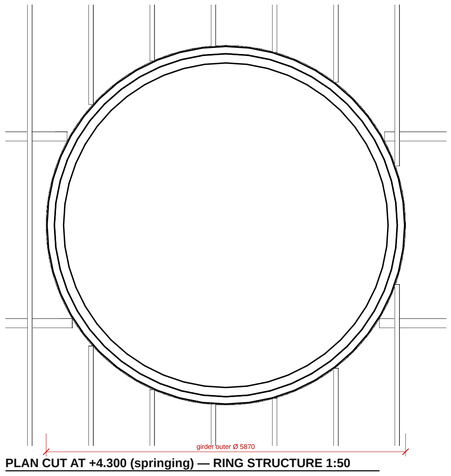

PLAN CUT AT +4.300 (springing) — RING STRUCTURE 1:50

ring beam + drum cut; curb, ring girder, beams and purlins below

BUILD-UP & ASSEMBLY SEQUENCE

1. Erect the ring girder (IPE 300 rolled, 4 segments) on temporary props; bolt the beam fin plates; check level against the 5 % roof plane.
2. Weld the C200 curb ring on the girder top flange; fix SHS 60 drum studs @ 600 (base plates 8 mm, 2xM12) and the top ring UPN 240 at +4.350.
3. Set the 24 rolled T80 ribs from the ring beam to the lantern ring (CHS 1016x10), bolted 2xM16 each end; brace with 2 hoops (L60).
4. Hang the karbandi GRC interior panels (precast from the 3D mould file) on M10 rods from the ribs; joint grout + tile touch-up.
5. Close the shell: GRC 25 mm segments on the ribs, waterproof membrane, glazed brick tiles in the ribbed pattern; lantern glazing and copper cap, finial.
6. Drum facing (kufic glazed brick), LED cove in the ring beam, chandelier hook test-loaded to 2 x SWL before hanging.

SAMARKAND — Uzbek / Tajik restaurant terrace · 254 Vo Nguyen Giap, Da Nang

Central dome C — section, ring plan, build-up

Drawn from the 3D model (closed-shell, QA-clean); dimensions in mm, levels in m from the finished terrace floor ±0.000

Sheet S-02 Rev R12-v5 2026-10-27 A1 Construction set — verify on site before fabrication
